




Design and Construction Update

Presentation to the Board of Education
April 12, 2021



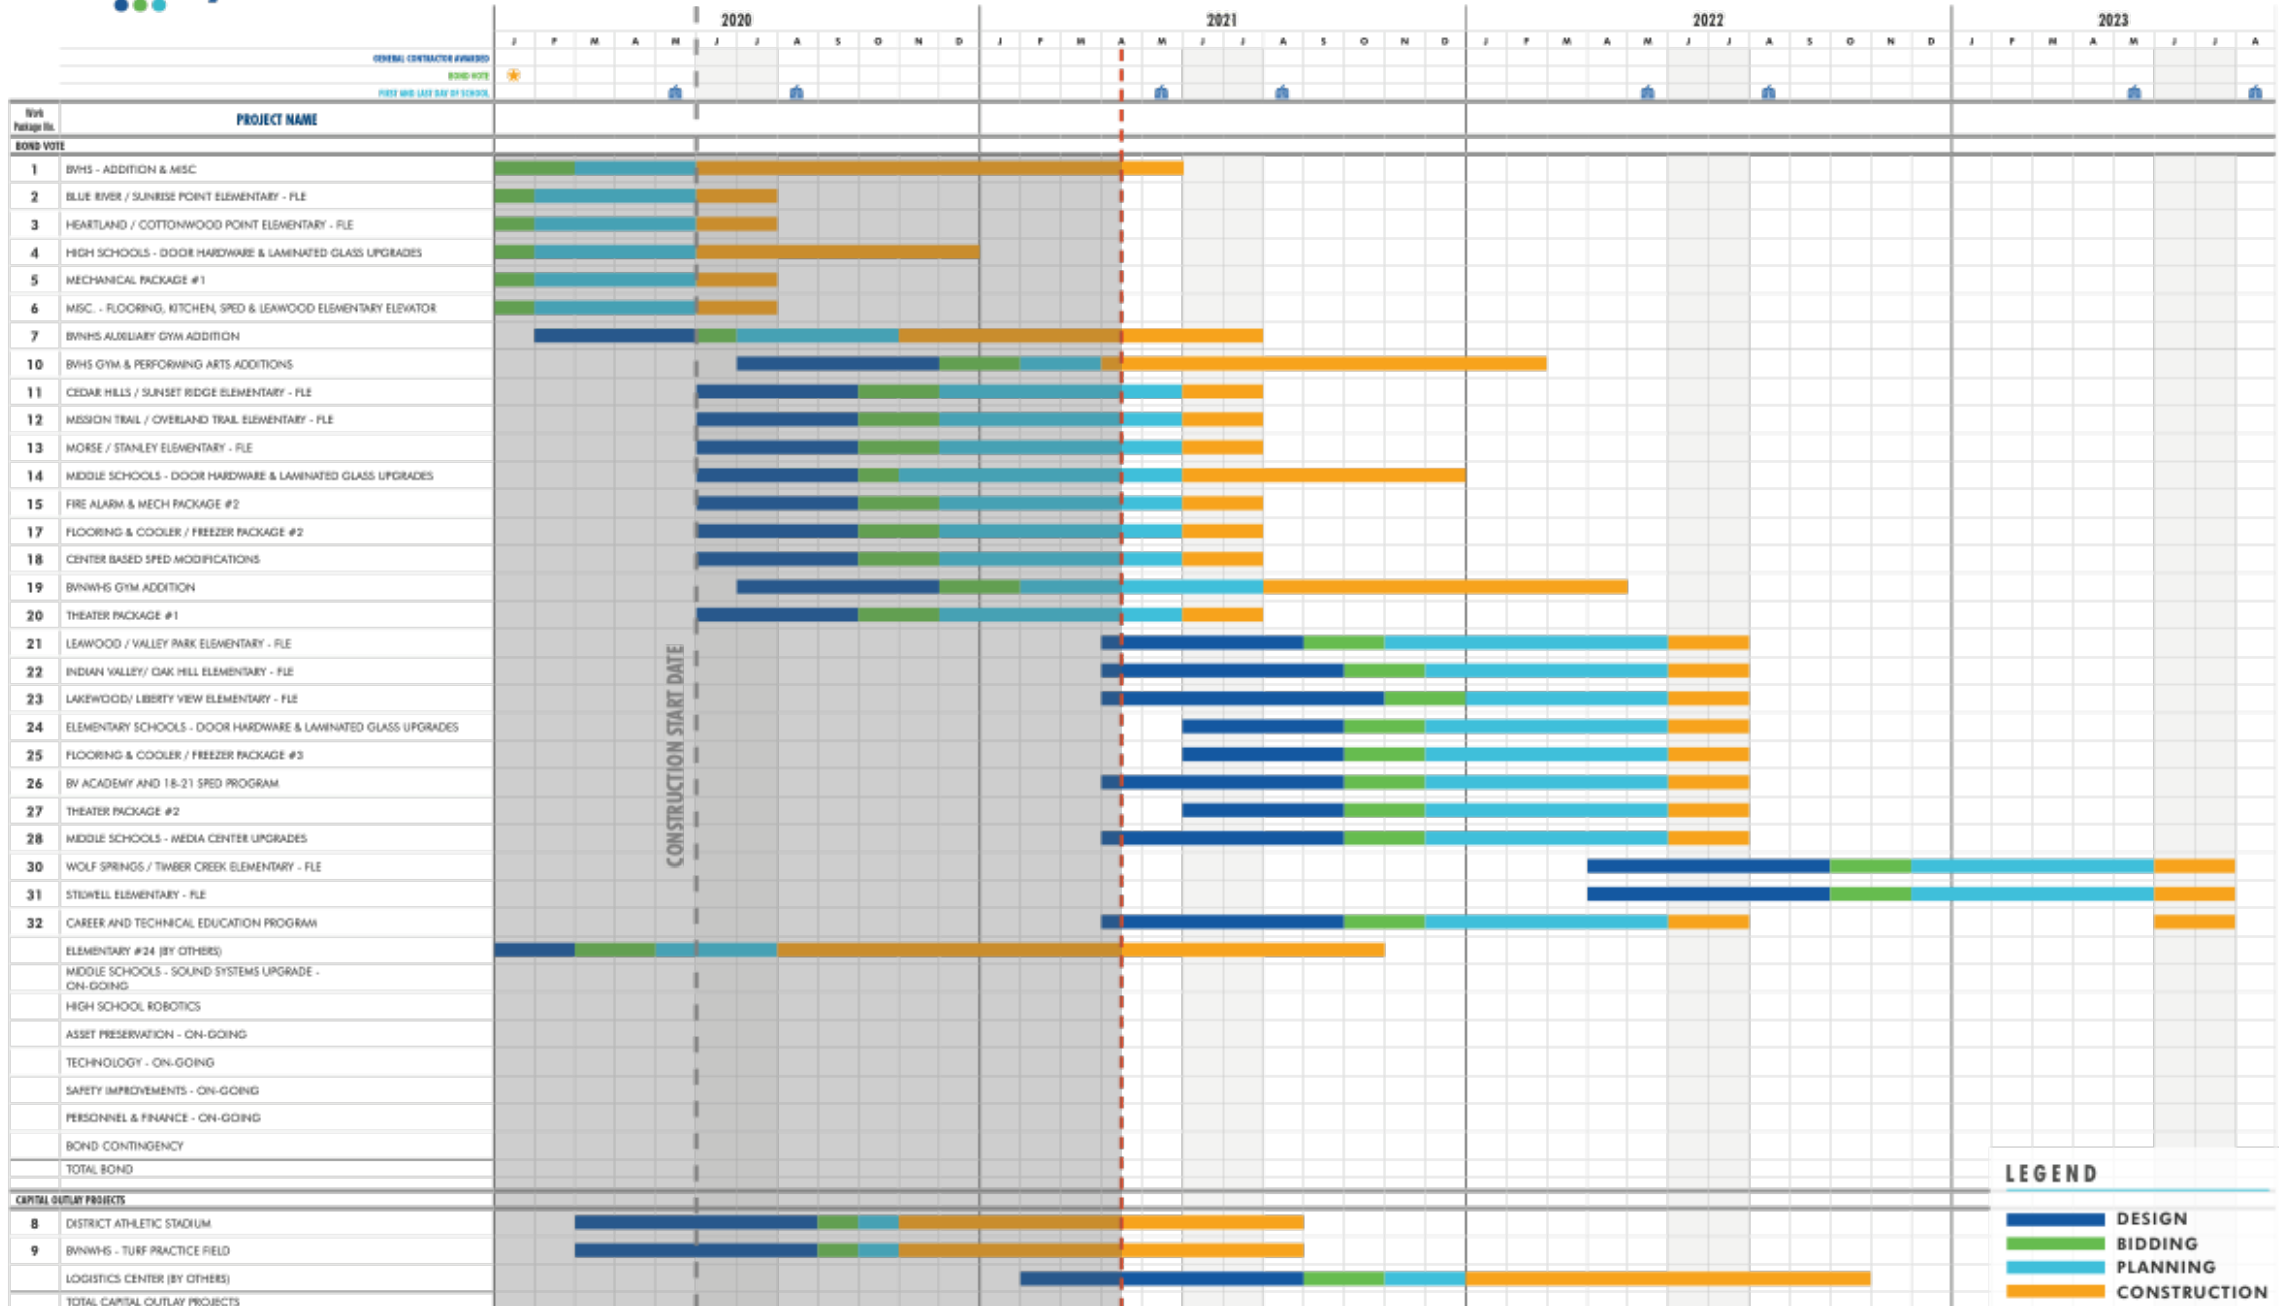

CONSTRUCTION START DATE

LEGEND

- DESIGN
- BIDDING
- PLANNING
- CONSTRUCTION

WP01 - BVH Addition

Construction Schedule: May 2020 to April 2021

Before



After



Scope: Remove 5 mobiles, build 12-classroom addition with 3 flex spaces

WP02, 03 - Elementary FLEs

Construction Schedule: Completed Summer 2020

Before



After



Scope: Renovate existing elementary schools (BRE, SPE, CPT, & HRT) to provide increased flexibility through operable walls

WP04 - HS Door Hardware and Laminated Glass

Construction Schedule: Completed Summer/Fall 2020



Scope: Provide thumbturn locks and impact resistant glass at classroom openings and other lockdown spaces

WP05 - Roofing and Major Mechanical

Construction Schedule: Completed Summer 2020



Scope: Replace end of life HVAC equipment and roofing at 7 sites totaling 50 unit replacements

WP06a - Flooring, Kitchen Cooler/Freezer, LES Elevator


Construction Schedule: Completed Summer 2020



Scope: Remove VCT tile and replace with polished concrete, repair pool deck, construct elevator at LES

WP06b - SPED Improvements at BVN, BVW, VPE

Construction Schedule: Completed Summer 2020

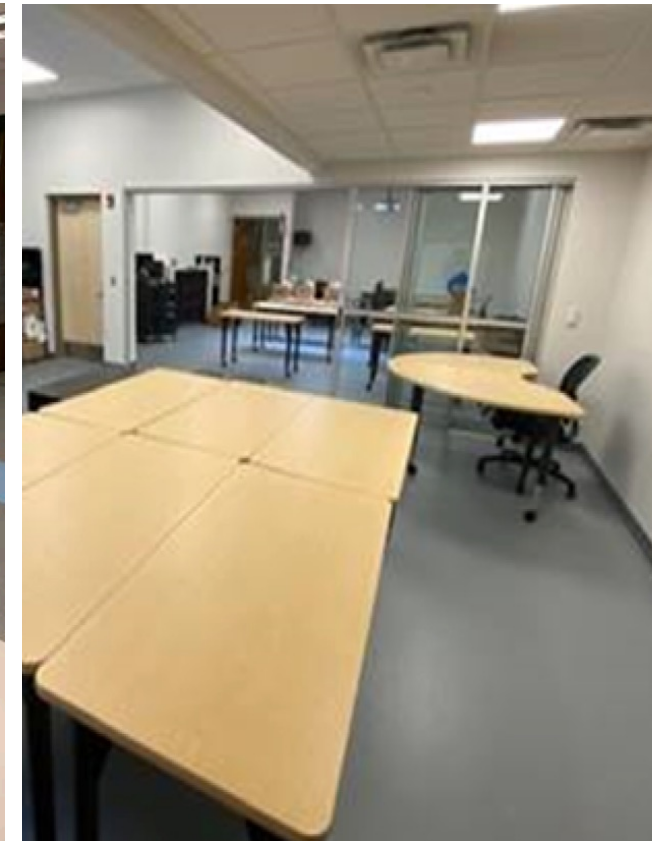

Scope: Renovate existing SPED spaces

WP07 - BVN Gymnasium Addition

Construction Schedule: November 2020 to July 2021

Before




Under Construction



Scope: Construct new 10,000sf, 425-seat auxiliary gymnasium, ICC-500 Storm Shelter

WP08 - Antioch District Activities Complex

Construction Schedule: November 2020 to August 2021

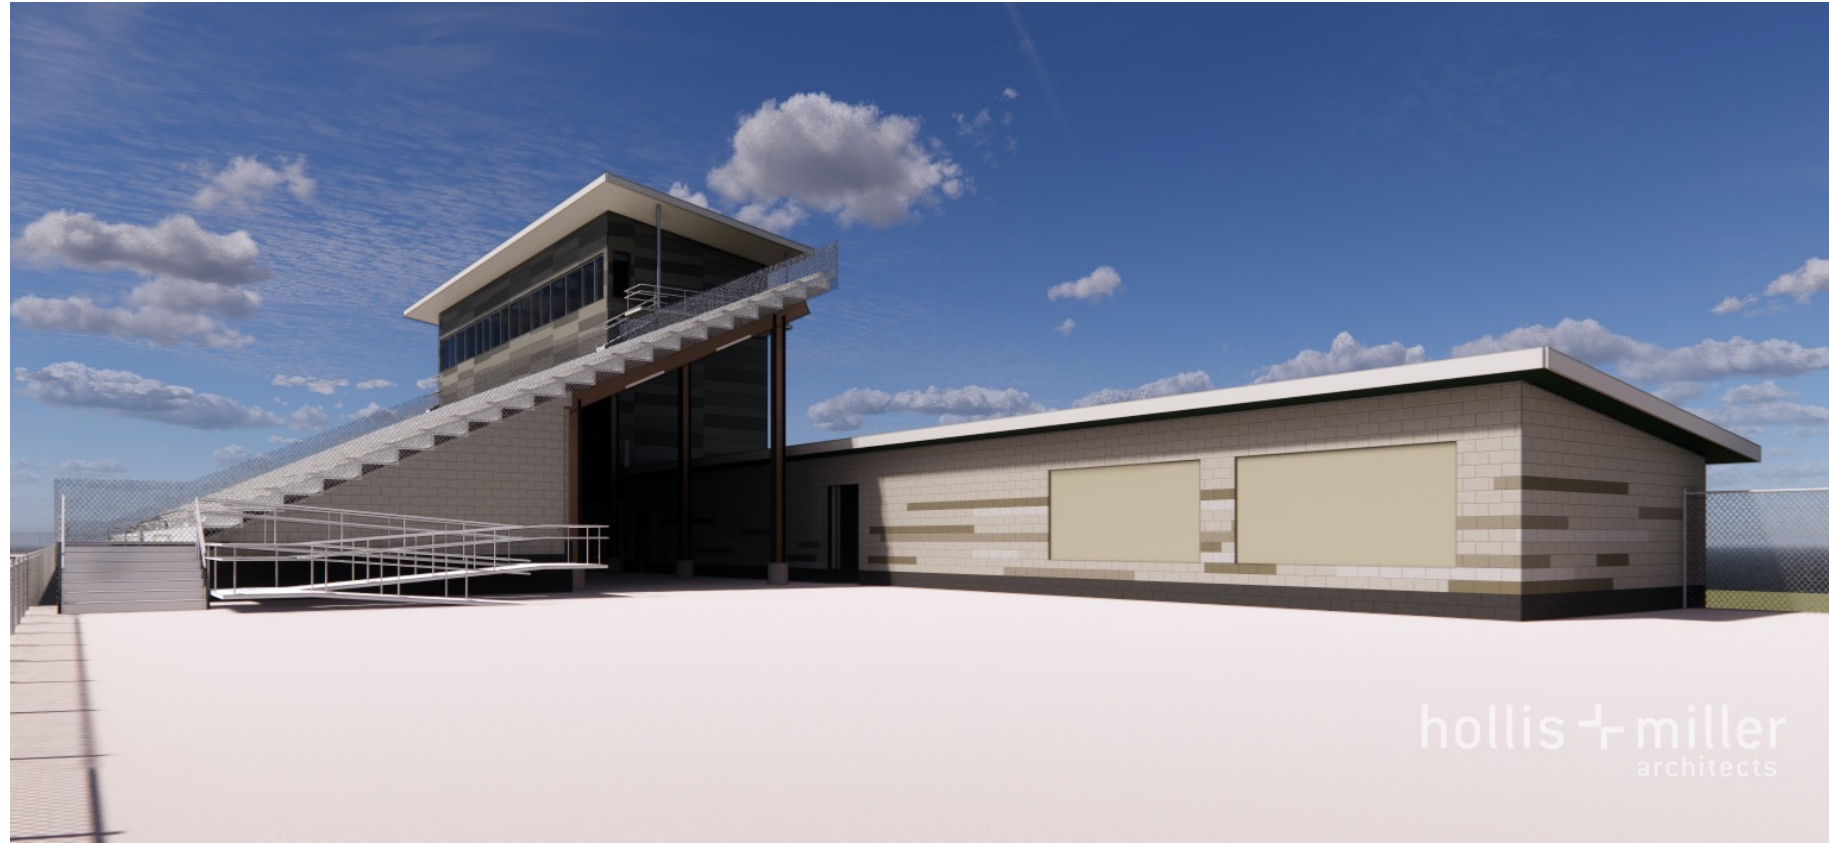

hollis + miller
architects

Scope: Construct new grandstand, bleachers, locker rooms, concessions, restrooms and storage at AntDAC



WP09 - BVNW Turf Practice Field

Construction Schedule: November 2020 to April 2021



Scope: Convert existing natural grass practice field into artificial turf field



Elementary #24



Scope: Construct new 67,000sf, 575-student elementary school with 24 classrooms, 3 dedicated SPED rooms, and flexible spaces throughout

Elementary #24




Scope: Construct new 67,000sf, 575 student capacity elementary school with 24 classrooms, 3 dedicated SPED rooms, and flexible spaces throughout

Upcoming Projects

Elementary FLEs: CHE, SRE, MTE, OTE, MOR, & STAN
Middle School Door Hardware and Laminated Glass
Miscellaneous Fire Alarm and Mechanical Upgrades
Miscellaneous Flooring and Kitchen Cooler/Freezer Upgrades
Center Based SPED Renovations
District Wide Theater Modifications and Safety Upgrades
BVH Gymnasium and Performing Arts Additions
BVNW High School Gymnasium Addition
Blue Valley Logistics Center

WP10 - BVH Gymnasium and Performing Arts Additions

Construction Schedule: April 2021 to March 2022

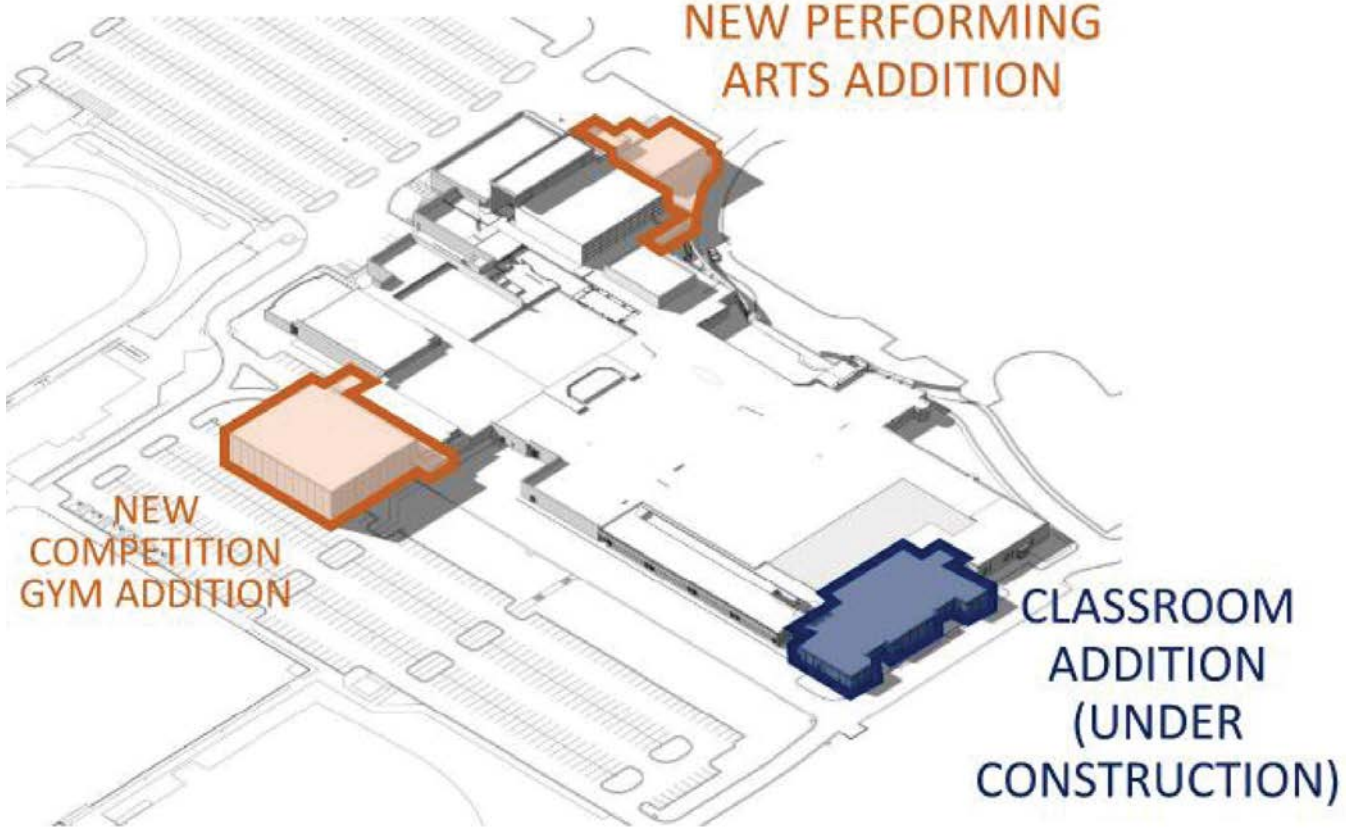

WP10 - BVH Gymnasium Addition


Construction Schedule: April 2021 to March 2022



Scope: Construct new 15,400sf, 2,000-seat competition gymnasium, ICC-500 Storm Shelter

WP10 - BVH Performing Arts Addition


Construction Schedule: April 2021 to March 2022

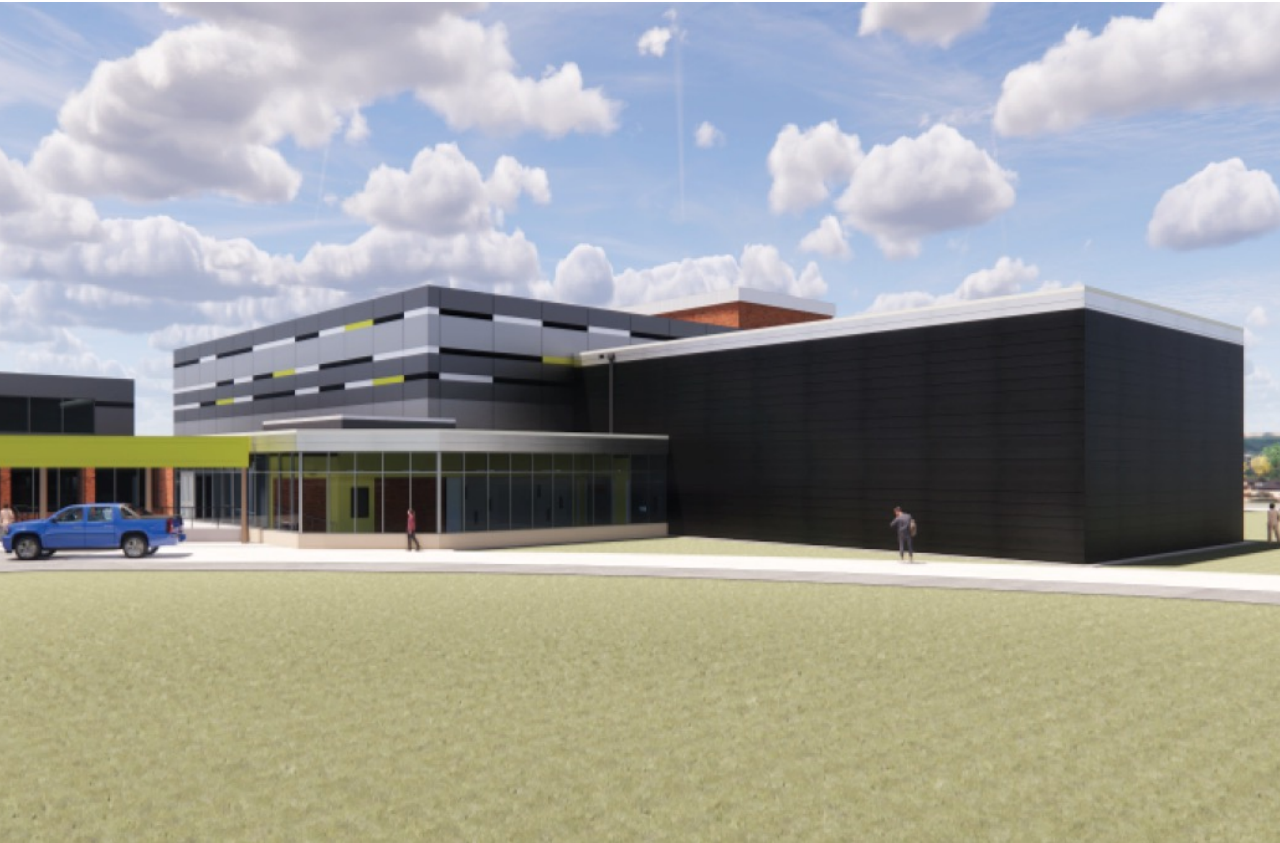

Scope: Construct new flexible theater, green room, practice rooms, storage and restrooms

WP19 - BVNW Gymnasium Addition

Construction Schedule: August 2021 to May 2022

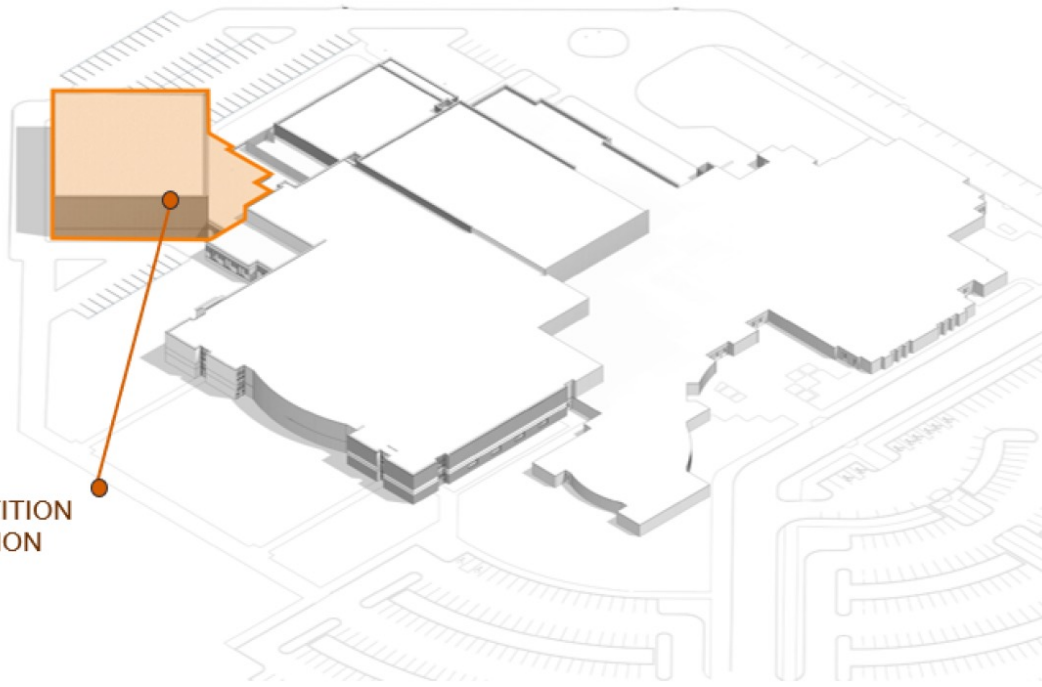


NEW COMPETITION
GYM ADDITION



Scope: Construct new 15,400sf, 2,000-seat competition gymnasium, ICC-500 Storm Shelter

Blue Valley Logistics Center

Construction Schedule: January 2022 to November 2022

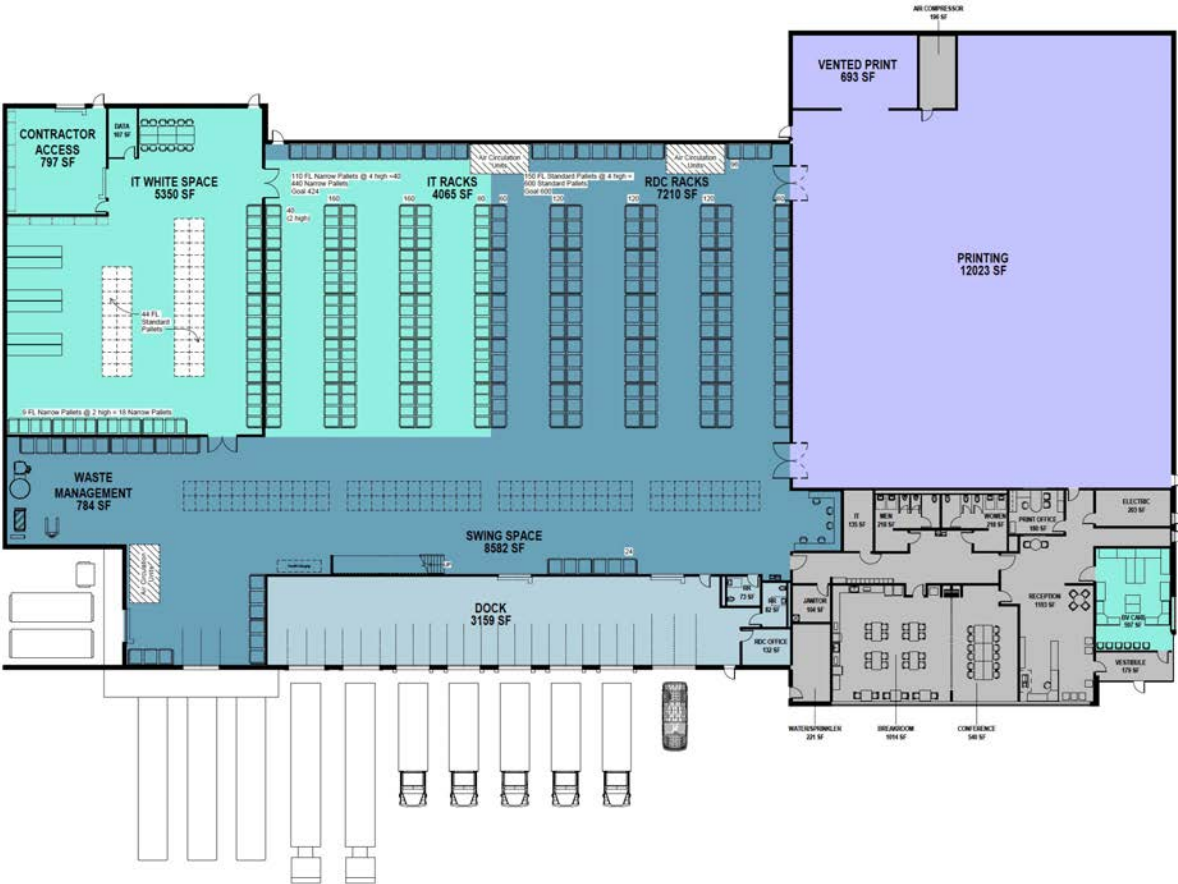

Scope: Construct new 50,000sf logistics center to house printing, shipping/receiving, IT white space, and 1:Learner device distribution



By the Numbers

Total Work Packages/Projects Bid to Date: 22

Total Project Sites: 75


Total Bond Project Budgets to Date: \$105,739,098

Total Approved GMPs to Date: \$105,227,628

Delta: (\$511,470) within .5%

Anticipated Unspent Contingency/Allowances Returned to Date:

\$663,854 (3 packages)

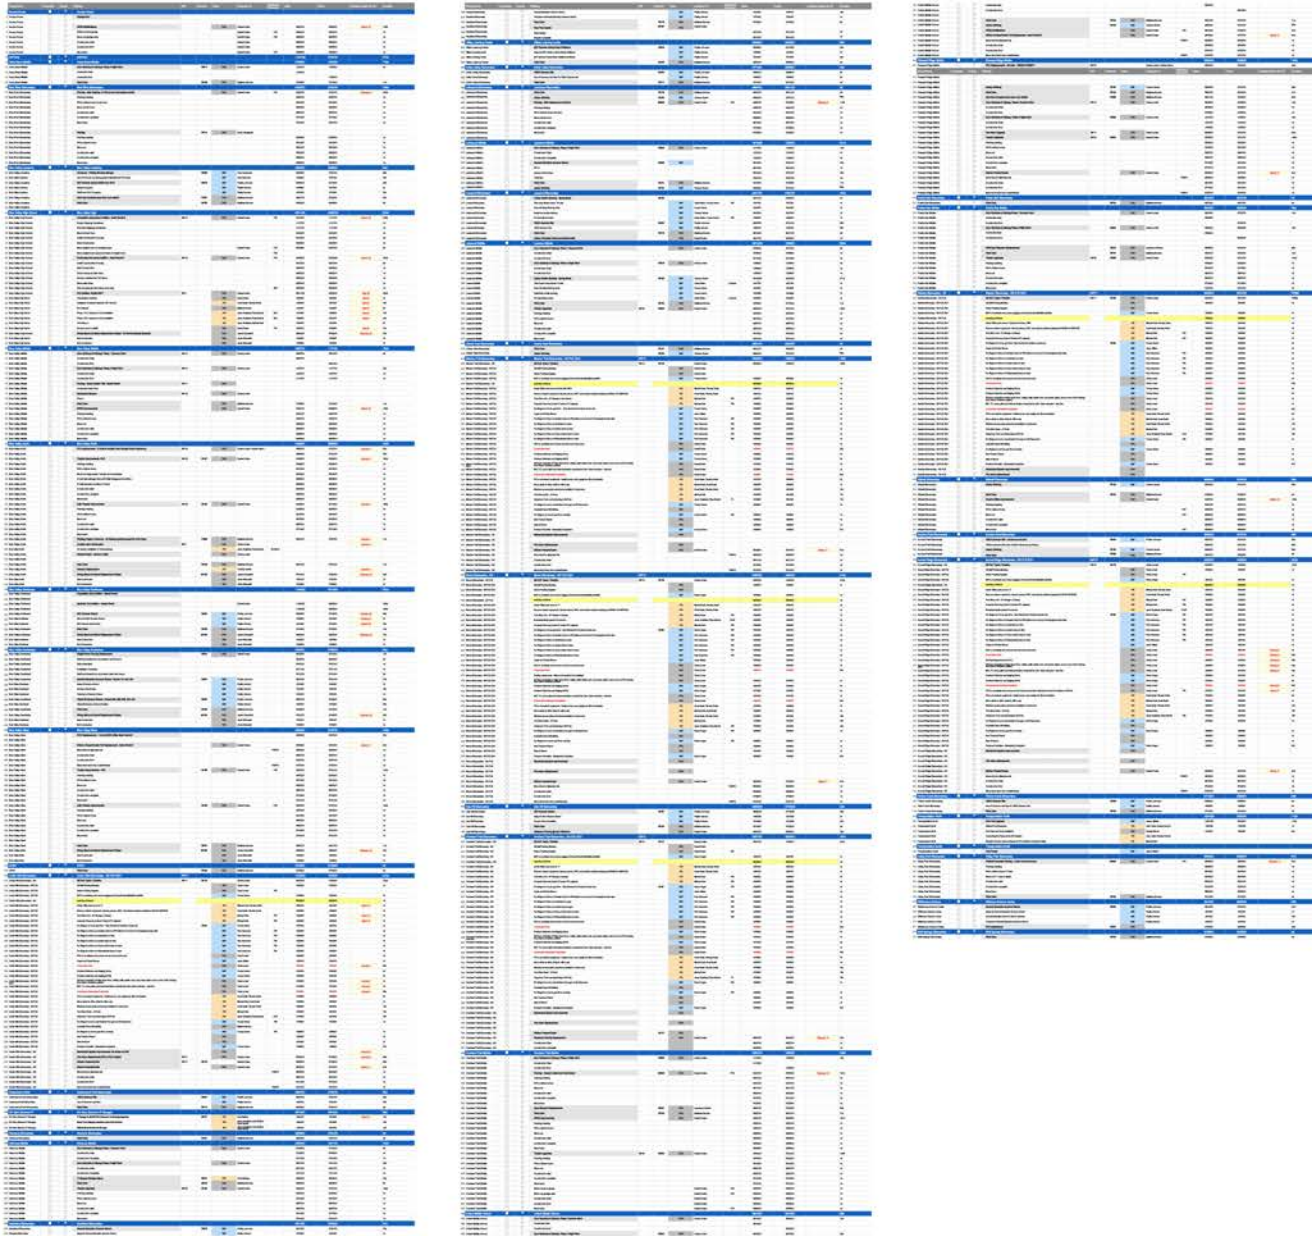

Thank You

blue BOND
2020 valley

